

Where the World Lands  
and Opportunities  
Take Off

# Clayton County SPL



# OST

Progress for Pennies

*Active Projects: September 2021*





## Clayton County Board of Commissioners

**Left to Right: Commissioner DeMont Davis (District 4),  
Commissioner Felicia Franklin (District 3),  
Chairman Jeffrey E. Turner,  
Commissioner Dr. Alika Anderson (District 1),  
Vice-Chair/Commissioner Gail B. Hambrick (District 2)**



## Library Improvements Districts 1, 2, 3 and 4

### Update: (Ongoing)

The Clayton County Library System contributes to the community and its citizens by offering services that meet their informational, educational, and leisure interests. There are six libraries located in the County with 2,992 library programs and over 1/2 million books. The Clayton County Library System is a member of GALILEO, Georgia's virtual library of full-text articles, e-books, journals, educational videos, and more.

Improvements and renovations to the Library Headquarters on Battle Creek Road include roof repairs, updated lighting, and painting the building exterior. The Morrow and Riverdale branch renovations include repairs to the walls and skylights.



Design Firm:  
Not Applicable



Construction Firm:  
Multiple



Project Completion:  
Not Applicable





# Modernization of Service Vehicle Fleet

## Districts 1, 2, 3 and 4

**Update: (Ongoing)**

Clayton County utilizes more than 700 vehicles in support of public safety operations, including first responder vehicles. As the age (6+ years) and mileage (100,000+) of our first responder vehicles increased, so did annual repair costs. Public safety concerns increased as our fleet aged.

Joint funding was approved to use SPLOST and capital funds to replace two hundred twenty-seven aging public safety vehicles. Priority was given based on vehicle age and mileage. Of the vehicles slated for replacement across the Police Department, Sheriff's Office, and Fire/EMS Department, 210 are funded by SPLOST funding.



**Design Firm:**  
Not Applicable



**Construction Firm:**  
Not Applicable



**Project Completion:**  
Not Applicable



# Welcome to Clayton County Signage & County Borders

## Districts 1, 2, 3 and 4

**Update: Site visits for signage placement are pending.**

Welcome to Clayton County! Where the World Lands and Opportunities Take Off.

New welcome signs will be strategically placed at the North, South, East, and West entrances of the County. The welcome signs will showcase the County's new brand and image to welcome and engage our citizens and visitors when entering the County, including the airport area.



**Design Firm:**  
To Be Determined



**Construction Firm:**  
To Be Determined



**Project Completion:**  
To Be Determined





## Full TV Station Remodel (CCTV-23) District 4

**Update: The finalization of equipment is on hold until the Administration Building studio design concept is complete.**

Under the Office of Communications, CCTV-23 is one of multiple communications channels used to provide educational, informative, and entertaining programming to citizens about the county's program, services, projects, plans, partnerships, and more.

The upgrade of equipment, lighting, set design, sound barriers, and the expansion of the studio location allows new educational segments and programming. These enhancements will strengthen the overall communication efforts of the county.



**Design Firm:**  
To Be Determined



**Construction Firm:**  
To Be Determined



**Project Completion:**  
To Be Determined



# Small Business Incubator & Records Center District 1

**Update: Pending.**

The Small Business Incubator will provide resources to introduce, connect, support, and expand new businesses in Clayton County to bolster the creation of jobs, investment, and economic development.

Combined with the County's Record's Center Building SPLOST initiative, this center provides public access to County records and historical information. The building will provide a Class-A office building space at the entrance to Clayton State University to attract and house multiple businesses and economic development activities. Reflecting the urban design at University Station, this development includes retail space for a coffee shop/bookstore and restaurant/cafe near Clayton State University.



**Design Firm:**  
To Be Determined



**Construction Firm:**  
To Be Determined



**Facility Open:**  
To Be Determined





# Fire Station Number 9 District 1

**Update:** The project is pending a station design work authorization request from the architect and engineer.

The design of Fire Station 9 will emulate the best features and functional characteristics of state-of-the-art fire stations. This model fosters an environment of development and growth. The new station will have enhanced safety measures to ensure the long-term health of our firefighters.

Features of the new fire station will include:

- Tactical Medical Team
- Search and Rescue Team
- Community Emergency Response Team
- Community Treatment Unit
- Fitness/Wellness Program.



**Design Firm:**  
To Be Determined



**Construction Firm:**  
To Be Determined



**Facility Open:**  
To Be Determined





## Correctional Facilities Renovations District 4

**Update: This project is 75% complete. The contractor is completing final interior finishes and exterior site concrete.**

The Clayton County Prison, located in Lovejoy, has a current capacity of 242 inmates. The mainly medium to minimal risk inmates are housed in an open dormitory setting and can participate in work-detail and custodial positions with various Clayton County government agencies.

This project includes the construction of a new dormitory, visitation room, and medical services area. A new transitional area will provide twenty-five beds for work-release inmates. Improvements to the building's interior and exterior infrastructure are slated.



**Design Firm:**  
Brown Design Group



**Construction Firm:**  
Scott Contracting



**Facility Open:**  
Fall 2021



# Modernization of Public Safety Fleet

## Districts 1, 2, 3 and 4

### Update: (Ongoing)

Clayton County utilizes more than 700 vehicles in support of public safety operations, including first responder vehicles. As the age (6+ years) and mileage (100,000+) of our first responder vehicles increased, so did annual repair costs. Public safety concerns increased as our fleet aged.

Joint funding was approved to use SPLOST and capital funds to replace two hundred twenty-seven aging public safety vehicles. Priority was given based on vehicle age and mileage. Of the vehicles slated for replacement across the Police Department, Sheriff's Office, and Fire/EMS Department, 210 are funded by SPLOST funding.



**Design Firm:**  
Not Applicable



**Construction Firm:**  
Not Applicable



**Project Completion:**  
To Be Determined





# Flint River Community Center District 3

**Update: Warranty item repairs are in progress including, HVAC and water intrusion.**

Located on a 21-acre site on Flint River Road, the Flint River Community Center is a collaborative project between the Department of Senior Services and Parks and Recreation. Providing recreation and activities for multiple generations, the center features game rooms, exercise rooms, a multipurpose gym, and an outdoor splash pad. The center showcases, for the first time in Clayton County, a “Black Box Theater” designed for live performances with flexible staging and seating.



**Design Firm:**  
NELSON Wakefield Beasley & Associates



**Construction Firm:**  
Morgan Constructors, LLC



**Facility Open:**  
Spring 2021





# Parkland and Greenway Acquisition/Development Districts 1, 2, 3 and 4

**Update: (Ongoing)**

This project implements the recommendations from the 2008 Greenspace Master Plan. The development includes ball fields, a sports complex, park-managed woodlands, forestry areas, and trails.



**Design Firm:**  
To Be Determined



**Construction Firm:**  
To Be Determined



**Project Completion:**  
To Be Determined





# VIP Complex Renovations at International Park District 4

**Update:** This project is 93% complete. Stadium seating installation is on hold pending fabrication of new seats with a November delivery date. Interior painting is in progress.

Renovations of the VIP Complex at International Park integrate outdoor spaces while maintaining a multi-functional facility for arts and entertainment. Other enhancements include additional covered seating, event administrative space, dressing rooms, additional concessions, re-design of restrooms, backstage facilities, and vendor kiosks.




**Design Firm:**  
Winter Construction



**Construction Firm:**  
Winter Construction



**Facility Open:**  
Fall 2021

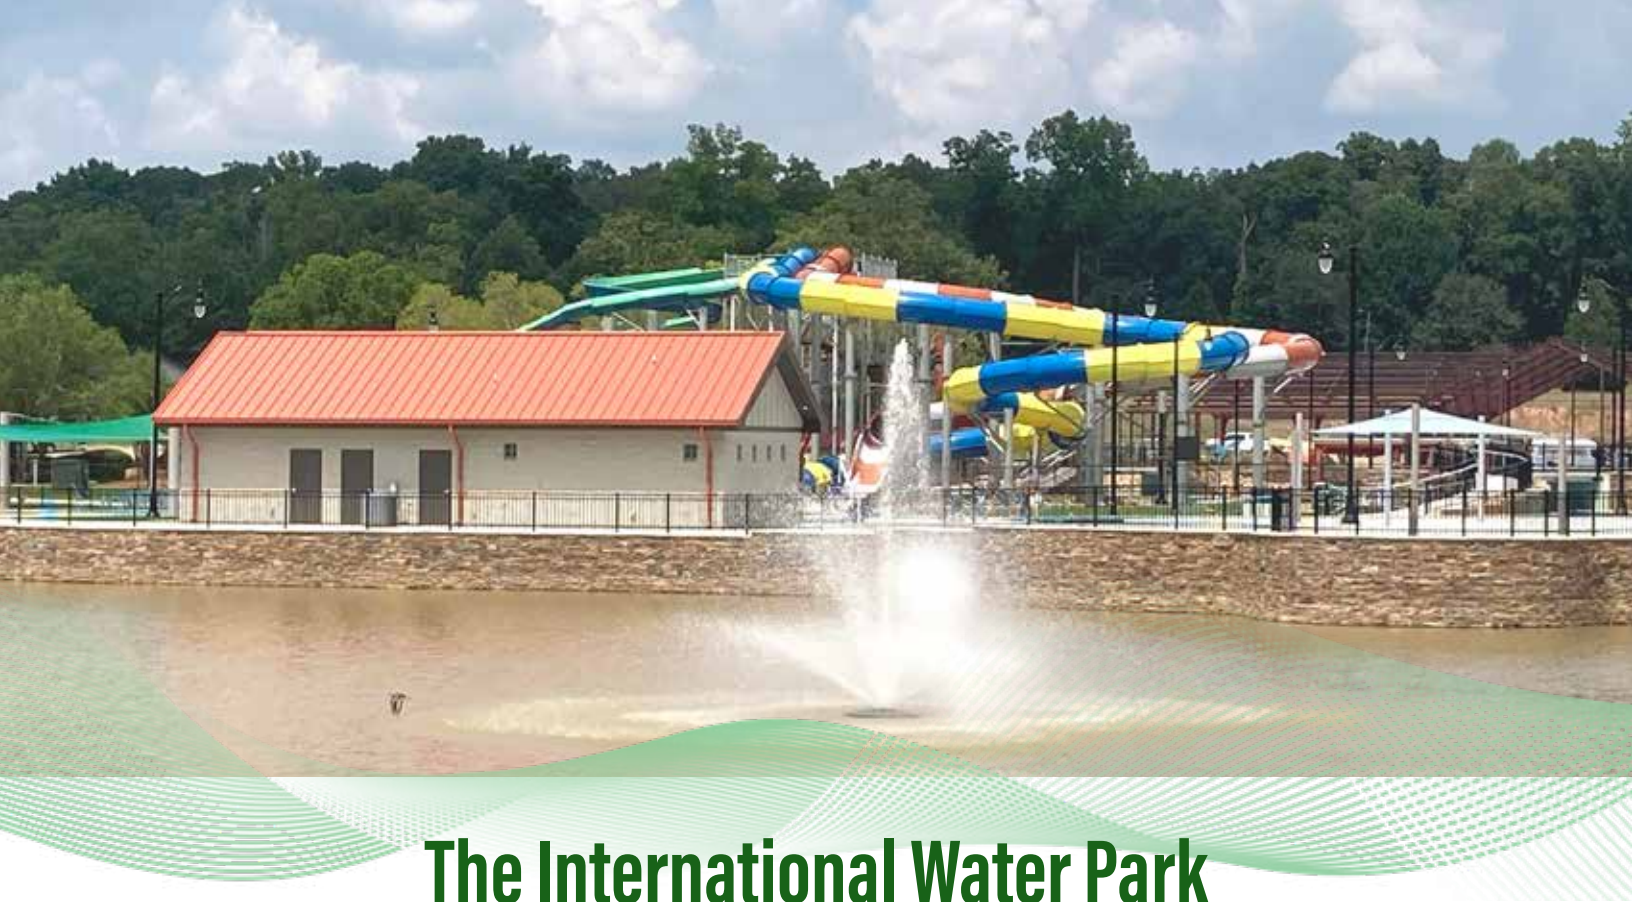

# The International Water Park

## District 4

**Update:** This project is 99% complete. The East parking lot light installation is complete, with parking lot resurfacing scheduled for early November.

The International Water Park renovation integrates outdoor spaces while maintaining a multi-functional facility. The International Water Park Improvements include:

- Sky Walk Adventure Climbing
- Boardwalk
- Food Truck Park
- Nassau Building renovation
- Dog Park
- New entrance
- Water Park with pools, splash pad, lazy river, waver runner, and kiddie pool
- Party Observation Deck
- Pavilions and cabanas overlooking the International Water Park



**Design Firm:**  
Integrated Construction and Nobility, Inc.



**Construction Firm:**  
Integrated Construction and Nobility, Inc.



**Facility Open:**  
Fall 2021





# Comprehensive Justice Management & Informational System Districts 1, 2, 3 and 4

## Update: (Ongoing)

This comprehensive criminal and civil judicial case management system provides reliable and modern infrastructure for all county judicial data and systems. This integrated system includes workflow automation, e-filing, case management, intelligent reporting, and customizable dashboards with statistical analysis. The cost for this multi-agency integrated solution includes hardware, data migration, training, and periodic system evaluation.



Design Firm:  
Not Applicable



Construction Firm:  
Not Applicable



Project Completion:  
To Be Determined

# Enterprise Resource Planning

## Districts 1, 2, 3 and 4

### Update: (Ongoing)

This integrated technology solution will replace antiquated, stand-alone systems for Finance, Human Resources, Tax Administration, Property Assessments, Business Intelligence, and Records Management. This solution will improve data management effectiveness through the provision of one central repository across county departments. This solution will also prompt a reduction in operating expenses and provide comprehensive data to improve strategic planning, decision-making, data analysis, and deliver clear and transparent reporting. The Tax Management Software System is included in this project.



**Design Firm:  
Not Applicable**



**Construction Firm:  
Not Applicable**



**Project Completion:  
To Be Determined**



# Upcoming Projects

**VIP Amphitheatre:** This project is in the design phase. Program needs and design concept are under review. Design by Gardner Spencer Smith Tench & Jarbeau; Construction Firm & Project Completion to be determined.

**Nassau Building:** This project is 45% complete. Exterior wall sheathing, exterior waterproofing, interior framing, exterior wall framing, and erection of the structural steel are complete. The installation of the metal roof is nearly complete with exterior wall sheathing, interior overhead mechanical installation, and interior framing in progress. This project includes the demolition of the old structure and the building of a new facility. Design and Construction by Brad Construction Company II; Project completion will be Fall 2021.

**County Records/Archive Phase II:** This project is 25% complete. Pending relocation of Voter's Registration, phased interior renovations will take place after the next two election cycles. Exterior wall pressure washing and prepping are complete, and a primer coat has been applied. Design Firm, Construction Firm & Project Completion to be determined.

**Board of Commissioners Administration Building:** The project is in the design phase. A three-story option has been selected and floor plans are under review. Design by Nelson Worldwide; Construction Firm to be determined; Project completion will be Winter 2024.

**County Fueling Center:** Print approval, building color, and signage renderings are all under review. Irrigation and landscape design are pending. Design by Pond & Company; Construction Firm to be determined; Project completion will be Winter 2022.

**Fire Station Number 15:** A design work authorization request is pending for the architect and engineer. Design Firm, Construction Firm & Project Completion to be determined.

## Widening and Reconstruction of Battle Creek Rd/Mt. Zion Blvd. - Districts 4

**Update:** As clearing continues east to Spring Place, erosion control measures are being installed.

This project includes the widening of Mt. Zion Boulevard just west of the intersections of Valley Hill Road Somerton Drive. The project widens Battle Creek Road at Mt. Zion Boulevard to a four-lane divided highway with a 20-foot wide median, sidewalks, and left and right turn lanes.



**Design Firm:  
To Be Determined**



**Construction Firm:  
To Be Determined**



**Project Completion:  
To Be Determined**

# Widening and Reconstruction of Battle Creek Road District 4

**Update:** The removal and disposal of stumps, roots, buried logs, and other debris are 80% complete. As clearing continues, erosion control measures are being installed.

The project includes the widening and re-construction of Battle Creek Road (CR 1342) from Valley Hill Road to Southlake Parkway for approximately 2.11 miles. This project widens Battle Creek Road from the existing two-lane facility to four lanes with a 20-foot wide raised median and urban shoulders including curb and gutter, a 2-foot wide grass strip, and 5-foot wide sidewalks.



**Design Firm:**  
Kimley-Horn & Associates, Inc.



**Construction Firm:**  
C. W. Matthews Contracting Co., Inc.



**Construction Firm:**  
To Be Determined

# Aviation Boulevard/Charles W. Grant Parkway District 2

**Update:** The beams are installed for the roadway bridge on the west side of the railroad line. Both bridges are 60%, complete with anticipated completion by early 2022. Construction on the final bridge road is anticipated to begin in mid-2022.

The proposed 4-lane facility widens and grades C.W. Grant Parkway under the Norfolk Southern Railroad and Old Dixie Highway. Also proposed is the widening and relocation of Conley Road and Old Dixie Road. The total length of the project is 1.30 miles.



**Design Firm:**  
Georgia Department of Transportation



**Construction Firm:**  
C. W. Matthews Contracting Co., Inc.



**Project Completion:**  
Spring 2023



# Brown Road Bridge Replacement District 3

**Update:** Authorization for the right-of-way phase is complete.

This project involves the replacement of the Brown Road Bridge over Swamp Creek.



**Design Firm:**  
**To Be Determined**



**Construction Firm:**  
**To Be Determined**



**Project Completion:**  
**To Be Determined**

# Valley Hill Road Bridge Replacement District 4

**Update:** All beams for the first phase of the project are in place. The contractor is placing drainage for the roadway widening.

This project involves the replacement of the Valley Hill Road Bridge over Flint River.



**Design Firm:**  
**WSP | Parsons Brinckerhoff**



**Construction Firm:**  
**CW Matthews Contracting Co., Inc.**



**Project Completion:**  
**To Be Determined**

# Clayton County

# SPL<sup>OST</sup>



## Progress for Pennies

Clayton County Board of Commissioners  
Office of Communications  
121 S. McDonough Street (Annex 2)  
Jonesboro, GA 30236  
[communications@claytoncountyga.gov](mailto:communications@claytoncountyga.gov)

Copyright @ 2021



*Where the World Lands  
and Opportunities  
Take Off*

[www.claytonsplost.com](http://www.claytonsplost.com)
